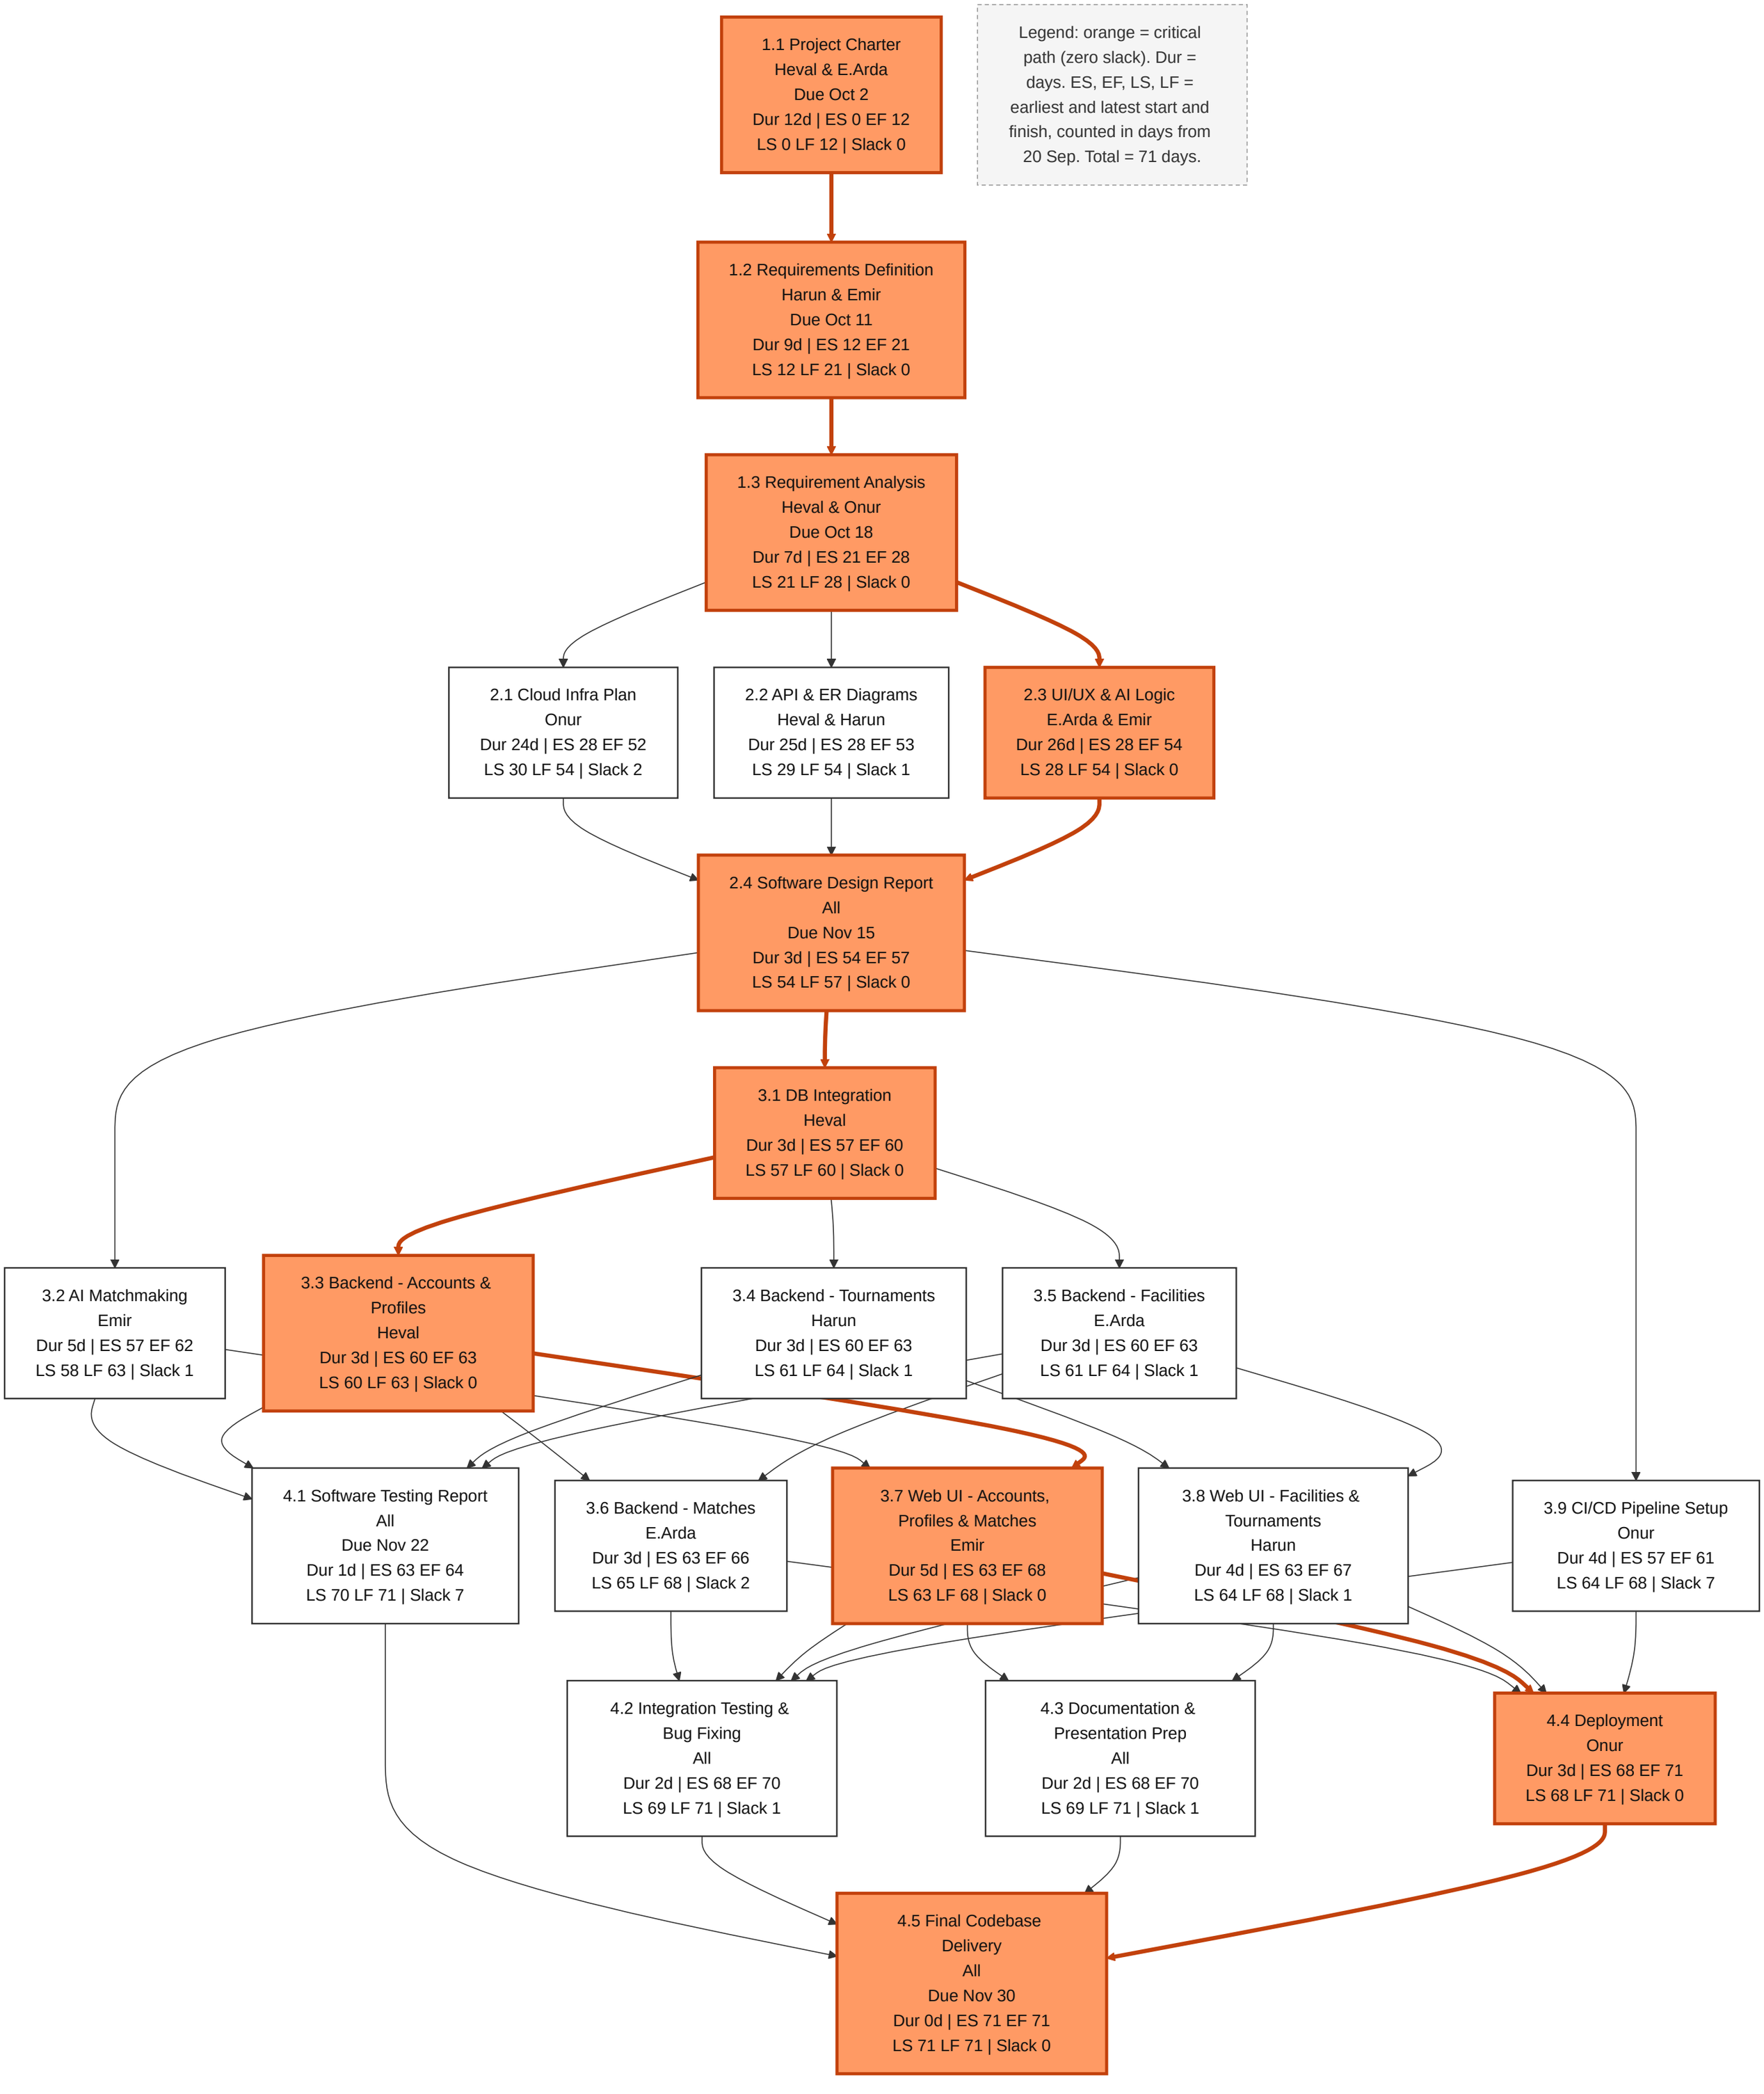
1.1 Project Charter
Heval & E.Arda
Due Oct 2
Dur 12d | ES 0 EF 12
LS 0 LF 12 | Slack 0
Legend: orange = critical path (zero slack). Dur = days. ES, EF, LS, LF = earliest and latest start and finish, counted in days from 20 Sep. Total = 71 days.
1.2 Requirements Definition
Harun & Emir
Due Oct 11
Dur 9d | ES 12 EF 21
LS 12 LF 21 | Slack 0
1.3 Requirement Analysis
Heval & Onur
Due Oct 18
Dur 7d | ES 21 EF 28
LS 21 LF 28 | Slack 0
2.1 Cloud Infra Plan
Onur
Dur 24d | ES 28 EF 52
LS 30 LF 54 | Slack 2
2.2 API & ER Diagrams
Heval & Harun
Dur 25d | ES 28 EF 53
LS 29 LF 54 | Slack 1
2.3 UI/UX & AI Logic
E.Arda & Emir
Dur 26d | ES 28 EF 54
LS 28 LF 54 | Slack 0
2.4 Software Design Report
All
Due Nov 15
Dur 3d | ES 54 EF 57
LS 54 LF 57 | Slack 0
3.1 DB Integration
Heval
Dur 3d | ES 57 EF 60
LS 57 LF 60 | Slack 0
3.2 AI Matchmaking
Emir
Dur 5d | ES 57 EF 62
LS 58 LF 63 | Slack 1
3.3 Backend - Accounts & Profiles
Heval
Dur 3d | ES 60 EF 63
LS 60 LF 63 | Slack 0
3.4 Backend - Tournaments
Harun
Dur 3d | ES 60 EF 63
LS 61 LF 64 | Slack 1
3.5 Backend - Facilities
E.Arda
Dur 3d | ES 60 EF 63
LS 61 LF 64 | Slack 1
4.1 Software Testing Report
All
Due Nov 22
Dur 1d | ES 63 EF 64
LS 70 LF 71 | Slack 7
3.6 Backend - Matches
E.Arda
Dur 3d | ES 63 EF 66
LS 65 LF 68 | Slack 2
3.7 Web UI - Accounts, Profiles & Matches
Emir
Dur 5d | ES 63 EF 68
LS 63 LF 68 | Slack 0
3.8 Web UI - Facilities & Tournaments
Harun
Dur 4d | ES 63 EF 67
LS 64 LF 68 | Slack 1
3.9 CI/CD Pipeline Setup
Onur
Dur 4d | ES 57 EF 61
LS 64 LF 68 | Slack 7
4.2 Integration Testing & Bug Fixing
All
Dur 2d | ES 68 EF 70
LS 69 LF 71 | Slack 1
4.3 Documentation & Presentation Prep
All
Dur 2d | ES 68 EF 70
LS 69 LF 71 | Slack 1
4.4 Deployment
Onur
Dur 3d | ES 68 EF 71
LS 68 LF 71 | Slack 0
4.5 Final Codebase Delivery
All
Due Nov 30
Dur 0d | ES 71 EF 71
LS 71 LF 71 | Slack 0
